



An update on the delivery of Crossrail west stations, being upgraded for Elizabeth line services

We have been making good progress across all of the Crossrail west stations, working towards a completion date in December 2020. We have nearly completed the Driver Only Operated (DOO) CCTV system across the stations as well as the platform extensions ready for the new, longer Elizabeth line trains.

At **Ealing Broadway** we have converted the female toilets into separate male and female facilities. This is so we can demolish the current male facilities to make way for the lifts, allowing step free access from street to platform.

At **Iver, Langley, Burnham, Taplow and Twyford** we have made good progress on the DOO CCTV system through the installation of cameras, cabling and power supply.

At **Maidenhead** we have almost completed the platform extensions on Platforms 2, 3, 4, and 5.

At **West Ealing** we have started the construction of the foundations for the main station building.



Toilets being refurbished at Ealing Broadway

At **Slough** we have now completed the DOO and we have almost completed the extensions to Platform 2, 3, 4 and 5 (including lighting).



West Drayton platform extensions



DOO cameras being installed

Driver Only Operated (DOO)

The DOO CCTV is a safety critical CCTV system that enables video signals captured from platform cameras to be transmitted to the train driver's cab on the new Elizabeth line trains.

This enables the driver to monitor the platform as passengers embark and disembark from the train.



Works coming up in September

Location	What are we doing?
Acton Main Line	Starting to build the supporting wall to the east of the station, and the basement walls
Ealing Broadway	Demolishing the existing waiting room on Platform 4, and the concourse on the first floor. We will then commence the steel installation and installing platform 2/3 lift shaft.
West Ealing	Building the supporting wall at the station
Southall	Continuing the construction of the foundations for the main station building. We will also be installing the main steel for the footbridge.
Hayes & Harlington	Completing the DOO camera works on platforms 4/5.
West Drayton	Completing the installation of cabling on platform 2. As well as the drainage work on platform 5.
Iver, Langley, Burnham, Taplow, & Twyford	Iver - Completing the installation of DOO metal work and start testing. Langley - Testing of the DOO. Burnham - Installing cabling on all platforms. Twyford - Installing cabling on all platforms. Iver - completing the final part of the DOO works.
Slough	Commissioning of DOO on all platforms. Installing cabling between the SDN Cabinet (power supply cabinet) on platform 5, to cabinets on all platforms via the bridge. Platform 5 extension to be completed.
M Maidenhead	Installing temporary power through the subway. As well as Installing the DOO camera posts on all platforms and testing the system. We will also be completing platform extensions and platform lighting.

We're holding drop in sessions to talk about works at Acton, Ealing, Southall, Hayes & Harlington, and West Drayton in preparation for the Elizabeth line and new TfL Rail services from December 2019.

Please see further information on the next page.


Contact us

If you have a concern or to find out more information:

Email us at CRcrossrail@networkrail.co.uk

Call our 24-hour helpline on **03457 11 41 41**

More information can be found at the icons below:

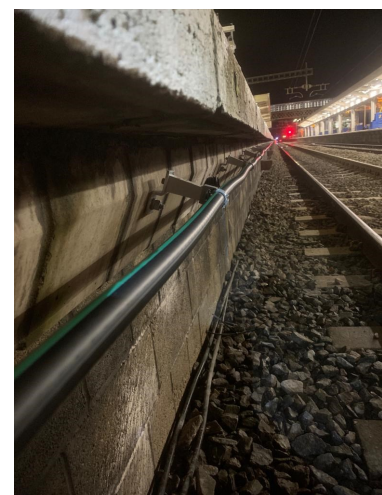

Cabling for the DOO



Crossrail West Stations Newsletter

September 2019

Putting
Passengers First

We're holding drop-in sessions to talk about improvement works at Stations in preparation for the Elizabeth line and new TfL Rail services from December 2019

Station	Venue	Date	Time
Acton Main Line	Holiday Inn London West, 4 Portal Way, Acton, London W3 6RT	Monday 16 September	17:00 – 19:30
West Drayton	St Matthew's Church, High Street, Yiewsley, Middlesex, UB7 7QH	Thursday 19 September	17:00 – 19:30
Hayes & Harlington	Hayes & Harlington Community Centre, Albert Rd, Hayes UB3 4HR	Wednesday 25 September	17:00 – 19:30
Ealing Broadway and West Ealing	Tefler Room, Ealing Town Hall, New Broadway, Ealing, London W5 2BY	Thursday 26 September	17:00 – 19:30
Southall	St George's Community Hall, 8-12 Lancaster Road, Southall UB1 1NW	Monday 30 September	17:30 – 20:00

Come along and talk to Network Rail, TfL, MTR and Crossrail about what this means for your station



Contact us

Call: 03457 11 41 41 Email: CRCrossrail@networkrail.co.uk

Visit: www.crossrail.co.uk



Working for you.
